



Inline Construction, Inc.
930 Jayhawk Rd
Marysville, KS 66508
Phone: 785-562-5525

Date: 8/4/2025

RE: Upcoming Street Work – Project Start Date: August 18, 2025

Dear Residents,

We are writing to inform you that street work will begin in your neighborhood starting **August 18, 2025**, with an anticipated duration of **approximately 240 calendar days, weather permitting**.

This project will involve **road reconstruction** and **storm sewer rehabilitation and replacement** to improve the infrastructure in your area. We understand this may cause temporary inconvenience and appreciate your patience and cooperation throughout the process.

Project Scope Includes:

- Approximately **5,100 SY** of 7" concrete pavement
- Approximately **2,700 LF** of curb and gutter
- Approximately **760 SY** of sidewalk and ADA-compliant ramps
- Installation of **13** storm sewer inlets and manholes
- Installation of approximately **500 LF** of storm sewer
- Replacement of **4** sanitary manholes


The work will be completed in **four phases**, as detailed in the attached phasing plan.

We are committed to minimizing disruptions and maintaining clear communication throughout the duration of the project. If you have any **questions or concerns**, please do not hesitate to contact us at the number listed above.

Thank you in advance for your understanding and support as we work to improve your neighborhood.


Sincerely,
Inline Construction, Inc.

2nd Street Phasing (Revised 7-30-25)

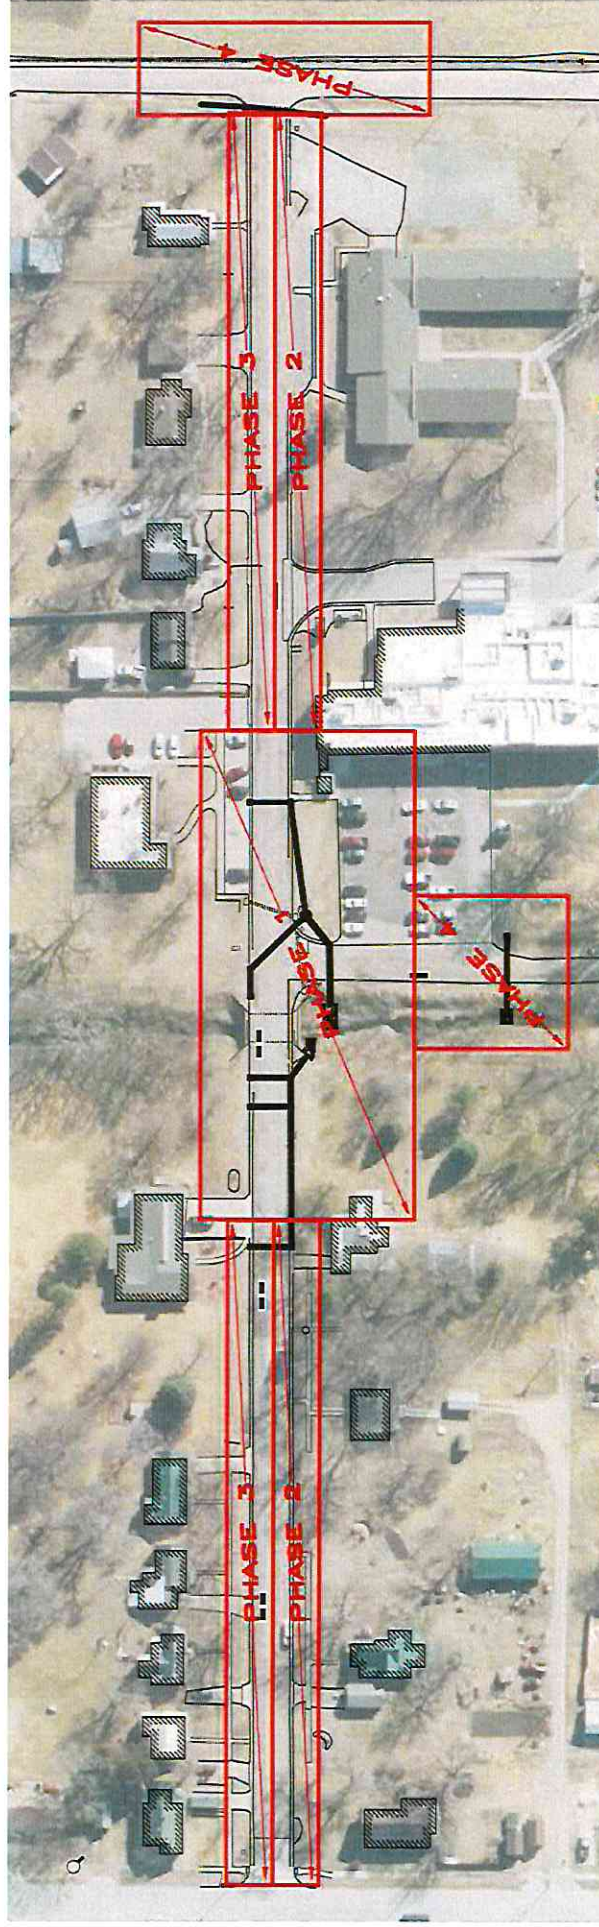


PHASE 1

- Repair Box Culvert
- Install Storm Sewer
- Rehab Sanitary Sewer Manhole at Sta 16+66.11 (Intersection of 2nd & A St.)
- Construct 2nd Street (full width) from:
 - Sta 15+00 (half of 214 E 2nd St. driveway) to Box culvert
 - Box culvert to Sta 18+51.71 (West side of Clinic driveway)
- Construct A Street (full width) from:
 - Sta 1+50 to 2+44.73
- Install Driveways
- Install Sidewalks

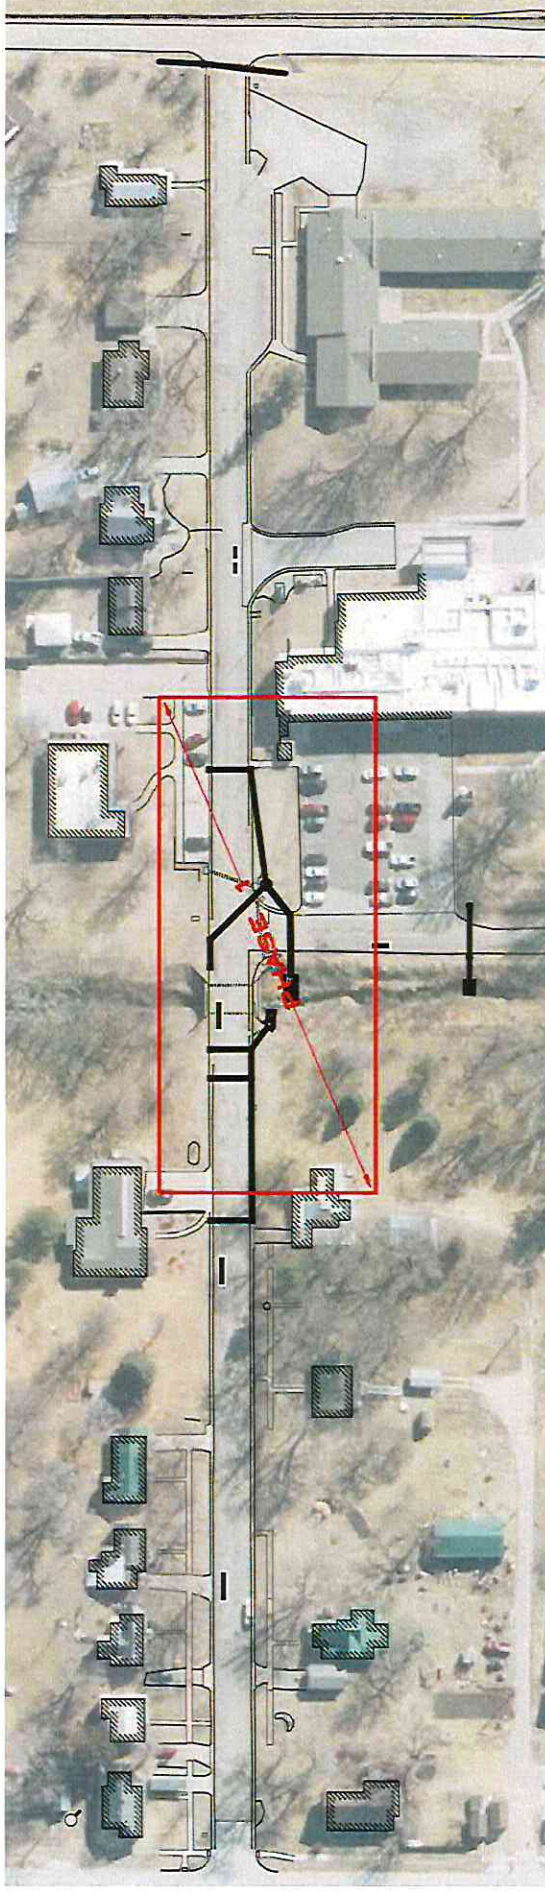


PHASE 2

- Install Storm Sewer
- Rehab Sanitary Sewer Manhole at Sta 13+41.13
- Construct 2nd Street (Eastbound Lane) from:
 - Sta 10+40 to Sta 15+00 (half of 214 E 2nd St. driveway)
 - Sta 18+51.71 (West side of Clinic driveway) to Sta 23+07.44
- Install Driveways
- Install Sidewalks

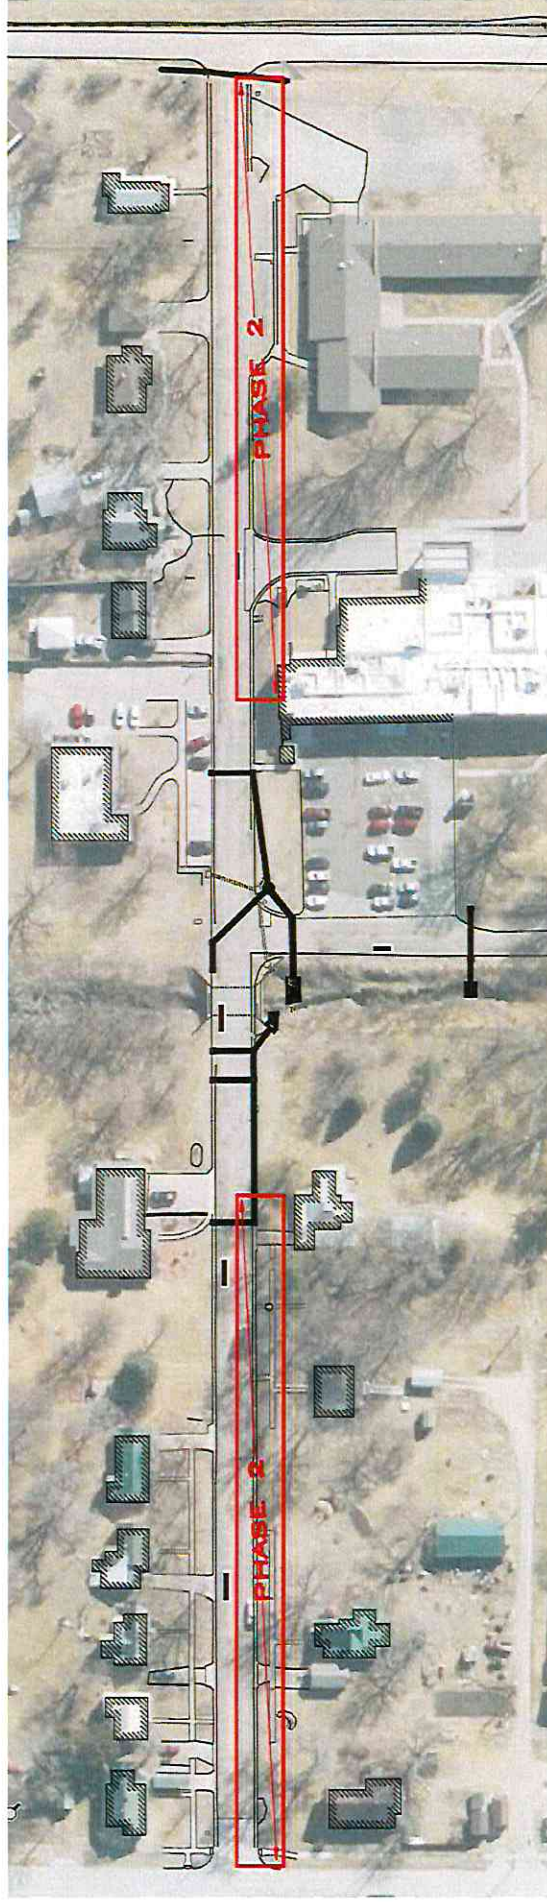

PHASE 3

- Install Storm Sewer
- Rehab Sanitary Sewer Manhole at Sta 19+64.39
- Rehab Sanitary Sewer Manhole at Sta 22+64.12
- Construct 2nd Street (Westbound Lane) from:
 - Sta 10+40 to Sta 15+00 (half of 214 E 2nd St. driveway)
 - Sta 18+51.71 (West side of Clinic driveway) to Sta 23+07.44
- Install Driveways
- Install Sidewalks

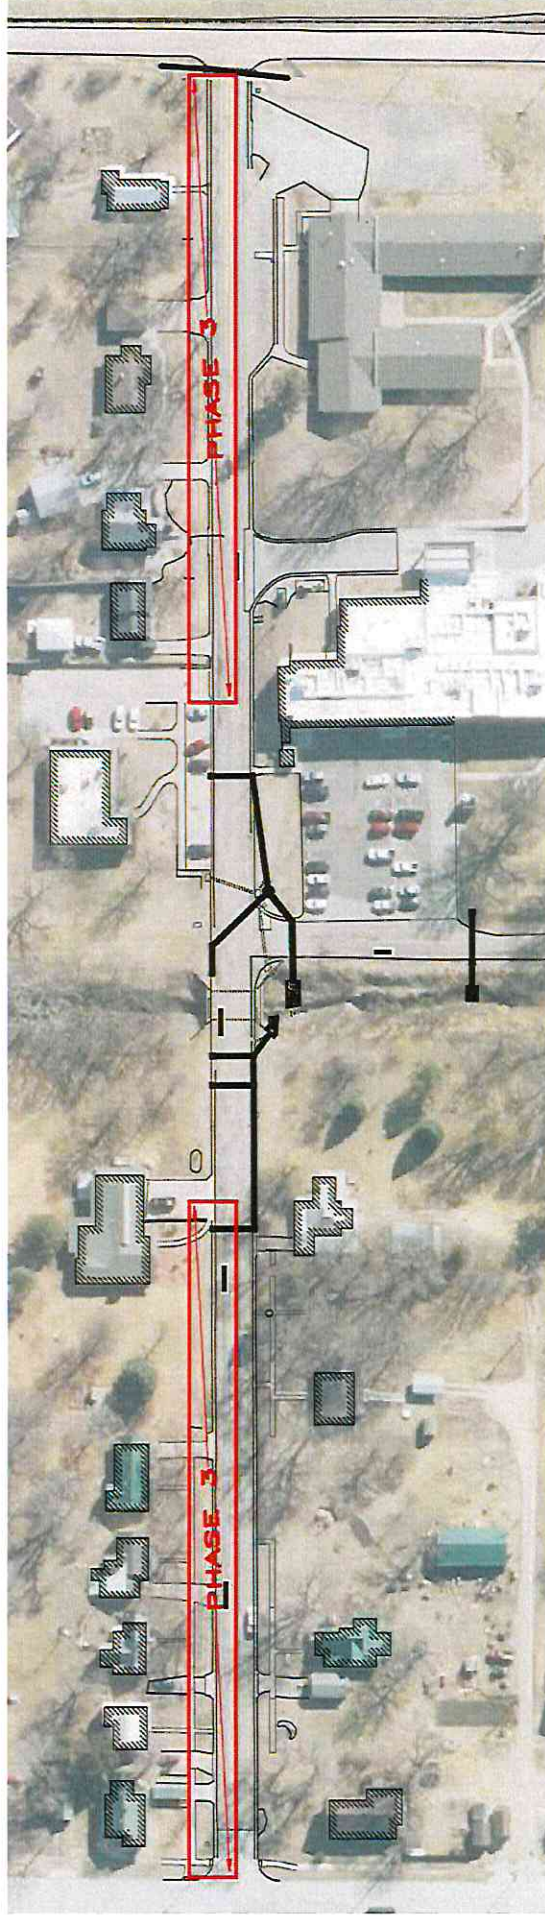

PHASE 4

- Install Storm Sewer
- Construct A Street (Westbound Lane) from:
 - Sta 0+50 to Sta 1+50
- Improve Pierce Rd as planned

